

SiyaBusa ERP

IMPLEMENTATION PROJECT PLAN

Sales Enablement

Masaphokati Technologies (Pty) Ltd

Document Version: 1.0

Effective Date: January 2026

Department: Professional Services

Classification: Internal

WE RULE. WE GOVERN. WE EMPOWER.

PROJECT MANAGEMENT

Standard implementation project plan template with phases and tasks.

Implementation Project Plan Template

Project Information

Field	Value
Project Name	SiyaBusa ERP Implementation - [Customer Name]
Customer	[Customer Name]
Project Manager (Provider)	[Name]
Project Manager (Customer)	[Name]
Start Date	[Date]
Target Go-Live	[Date]
Implementation Package	Quick Start Standard Advanced Enterprise

Table of Contents

1. [Project Overview](#)
2. [Project Methodology](#)
3. [Project Phases](#)
4. [Detailed Task List](#)
5. [Resource Plan](#)
6. [Communication Plan](#)
7. [Risk Register](#)
8. [Quality Assurance](#)
9. [Go-Live Checklist](#)

1. Project Overview

1.1 Project Objectives

#	Objective	Success Criteria
1	Deploy SiyaBusa ERP	System accessible to all users
2	Configure [X] modules	All modules functional per requirements
3	Migrate historical data	Data validated, balances reconciled
4	Train [X] users	All users certified on relevant modules
5	Go-live by [Date]	Production transactions processed
6	Achieve ROI targets	Measurable efficiency improvements

1.2 Scope Summary

Modules In Scope:

- Financial Accounting (GL, AP, AR)
- Bank Reconciliation
- Inventory Management
- Warehouse Management
- Sales & CRM
- Purchase Management
- HR & Payroll
- Manufacturing
- SARS Sentinel
- Audit Shield
- Other: _____

Integrations In Scope:

- Bank feeds: _____

- E-commerce: _____
- Other: _____


1.3 Project Timeline Overview

PROJECT TIMELINE						
Week 1	Week 2	Week 3	Week 4	Week 5	Week 6	Week 7+
INITIATE	CONFIGURE	CONFIGURE	DATA MIGRATE	TEST	TRAIN	GO-LIVE
Kickoff Plan Confirm Reqs	Core Modules Setup	Advanced Modules Setup	Extract Transform Load Validate	System Test UAT	Admin Training User Training	Final Prep Go-Live Support

2. Project Methodology

2.1 Implementation Approach

SiyaBusa follows an **Agile-Waterfall Hybrid** approach:

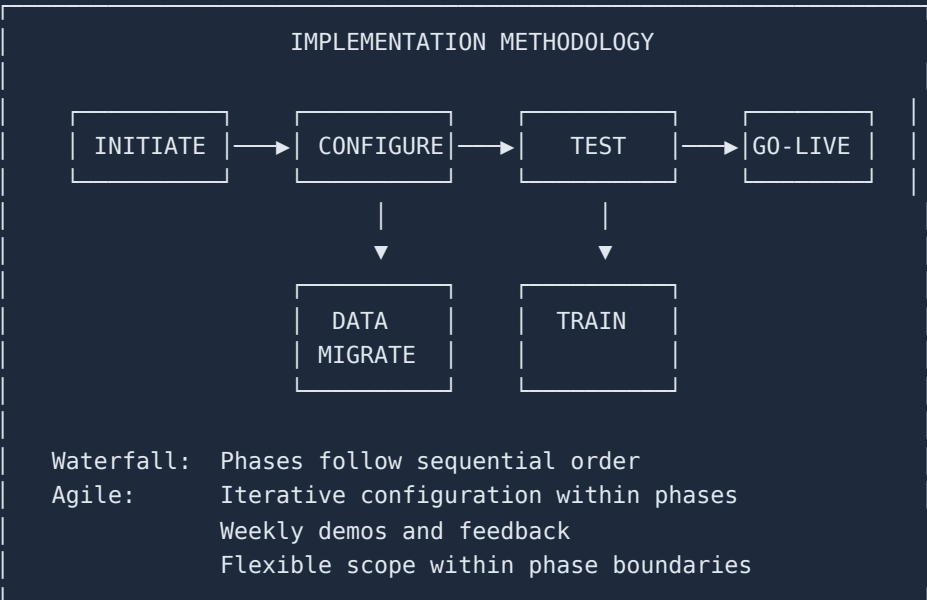

2.2 Key Principles

Principle	Description
Iterative Configuration	Configure, demo, refine in weekly cycles
Early Testing	Test throughout, not just at the end
Change Control	Formal process for scope changes
Knowledge Transfer	Customer self-sufficiency as goal
Data-First	Data quality determines success

3. Project Phases

Phase 1: Initiation (Week 1)

Objective: Establish project foundation and confirm requirements

Deliverable	Description	Owner
Project Kickoff	Align teams, set expectations	Provider PM
Project Plan	Detailed schedule, resources	Provider PM
Requirements Document	Confirmed configuration decisions	Provider Consultant
Data Requirements	Data mapping, migration plan	Provider Consultant
Communication Plan	Meeting cadence, contacts	Provider PM

Key Activities:

1. Conduct kickoff meeting with all stakeholders
2. Review and confirm business requirements
3. Define Chart of Accounts structure
4. Document current business processes
5. Identify data sources and quality
6. Establish project infrastructure (project site, tools)
7. Create detailed project schedule

Exit Criteria:

- Kickoff completed
- Requirements signed off
- Project plan approved
- Data assessment complete

Phase 2: Configuration (Weeks 2-3)

Objective: Configure SiyaBusa to meet business requirements

Week 2: Core Configuration

Module	Configuration Tasks	Owner
Company Setup	Company details, fiscal year, currency, tax settings	Provider
Chart of Accounts	Account structure, account types, reporting hierarchy	Provider
General Ledger	Journals, templates, reporting periods	Provider
User Setup	Roles, permissions, user accounts	Provider
SARS Sentinel	VAT setup, PAYE configuration	Provider

Week 3: Module Configuration

Module	Configuration Tasks	Owner
Accounts Payable	Supplier setup, payment terms, aging, approvals	Provider
Accounts Receivable	Customer setup, credit terms, aging, statements	Provider
Inventory	Products, categories, UOM, pricing, warehouses	Provider
Sales	Quote/Order/Invoice workflows, document templates	Provider
Purchasing	PO workflows, receiving, three-way match	Provider
HR & Payroll	Pay structures, deductions, leave policies	Provider

Key Activities:

1. Configure company settings

2. Import/create Chart of Accounts
3. Set up tax configuration (VAT, PAYE)
4. Configure user roles and permissions
5. Set up master data (customers, suppliers, products)
6. Configure document templates (invoices, POs, quotes)
7. Set up approval workflows
8. Configure integrations
9. Weekly demo to customer for feedback


Exit Criteria:

- All modules configured
 - Configuration reviewed and approved
 - Test transactions successful
 - Integration connectivity confirmed
-

Phase 3: Data Migration (Week 4)

Objective: Migrate historical data accurately

Data Migration Stages:

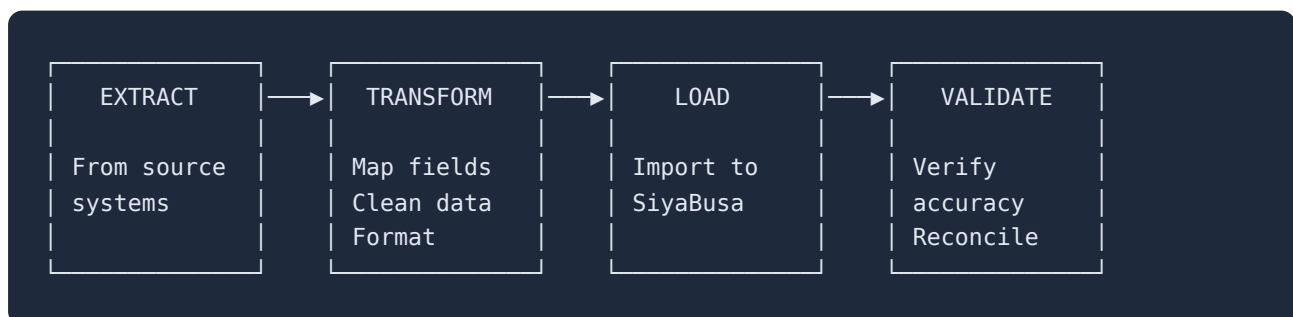

Data Types:

Data Type	Records	Source	Migration Method
Chart of Accounts	[X]	[Source]	Template
Customers	[X]	[Source]	API/Template
Suppliers	[X]	[Source]	API/Template
Products	[X]	[Source]	API/Template
Opening Balances	As of [Date]	[Source]	Journal
Historical Transactions	[X] years	[Source]	Bulk import
Employees	[X]	[Source]	Template

Key Activities:

1. Extract data from source systems
2. Map data to SiyaBusa fields
3. Cleanse and transform data
4. Perform test migration
5. Validate test migration results
6. Perform final migration
7. Reconcile balances to source

Exit Criteria:

- All data migrated
- Trial balance reconciled
- Customer/supplier balances verified
- Inventory counts reconciled
- Customer sign-off on data accuracy

Phase 4: Testing (Week 5)

Objective: Verify system functions correctly

Testing Types:

Test Type	Description	Responsibility
System Testing	Technical functionality	Provider
Integration Testing	Integrations work correctly	Provider
User Acceptance Testing	Business scenarios work	Customer
Regression Testing	Changes don't break existing	Provider

Test Scenarios:

#	Scenario	Steps	Expected Result	Status
T1	Create Customer Invoice	New invoice → Approve → Post	Invoice posted, GL updated	
T2	Receive Supplier Invoice	Enter bill → Match PO → Approve	Bill recorded, AP updated	
T3	Process Payment	Select invoices → Generate payment	Payment recorded, bank updated	
T4	Stock Receipt	Receive goods → GRN → Update stock	Inventory increased	
T5	Sales Order → Invoice	SO → Pick → Ship → Invoice	Full cycle complete	
T6	Payroll Run	Process payroll → Review → Approve	Payslips generated	
T7	VAT Return	Generate VAT201 → Review	Accurate VAT report	
T8	Month-End Close	Run close → Generate reports	Financials accurate	

Key Activities:

1. Execute system test cases
2. Execute integration test cases
3. Customer executes UAT scenarios
4. Log and track issues
5. Resolve critical/high issues
6. Re-test resolved issues
7. Obtain UAT sign-off

Exit Criteria:

- All P1/P2 issues resolved
 - P3 issues documented with workarounds
 - UAT sign-off obtained
 - Performance acceptable
-

Phase 5: Training (Week 6)

Objective: Enable users to operate the system effectively

Training Schedule:

Day	Time	Module	Audience	Duration
Mon	09:00	System Admin	IT/Admin	4 hours
Mon	14:00	System Admin	IT/Admin	4 hours
Tue	09:00	Financial Accounting	Finance	4 hours
Tue	14:00	AP/AR	Finance	4 hours
Wed	09:00	Inventory/Sales	Operations	4 hours
Wed	14:00	Purchasing	Procurement	4 hours
Thu	09:00	HR & Payroll	HR	4 hours
Thu	14:00	Reporting	Finance/Mgmt	2 hours
Fri	09:00	End User Overview	All Users	4 hours

Training Materials:

Material	Format	Delivery
User Guides	PDF	Shared portal
Quick Reference Cards	PDF	Printed/Digital
Video Tutorials	MP4	Shared portal
Exercise Workbooks	PDF	Training sessions
Assessment Quizzes	Online	Post-training

Key Activities:

1. Prepare training environment
2. Customize training materials for customer
3. Conduct admin training
4. Conduct module-specific training
5. Conduct end user training
6. Assess training effectiveness
7. Address training gaps

Exit Criteria:

- All users trained on relevant modules
- Training assessments passed (>80%)
- Super users identified and prepared
- Training materials delivered

Phase 6: Go-Live (Week 7)

Objective: Successfully transition to production use

Go-Live Timeline:

GO-LIVE WEEK					
Day -2	Day -1	DAY 0	Day +1	Day +2	Days +3 to +5
Final Prep	Data Cutover	GO LIVE	First Close	Issue Resolve	Stabilize Support
Final testing Comms	Final balances Cutoff	Users begin Support	Daily process Review	Fix issues Adjust	Monitor Handover Close out

Go-Live Support:

Support Level	Hours	Contact
On-Call (Day 0-1)	07:00-19:00	[Phone/Chat]
Extended (Day 2-5)	08:00-17:00	[Phone/Email]
Standard (After Day 5)	Normal support SLA	Support portal

Key Activities:

1. Complete go-live checklist (see Section 9)
2. Final data cutover
3. Deactivate old system (if applicable)
4. Go-live communication to users
5. Begin production transactions
6. Monitor system performance
7. Provide go-live support
8. Resolve issues as they arise
9. First day-end/period-end close
10. Handover to standard support

Exit Criteria:

- System live and stable
- Users transacting successfully
- No critical open issues

- First period close successful
- Handover to support complete

4. Detailed Task List

4.1 Phase 1: Initiation Tasks

ID	Task	Duration	Start	End	Owner	Status
1.1	Project kickoff meeting	2 hours			Provider PM	
1.2	Review business requirements	4 hours			Provider Consultant	
1.3	Document current processes	4 hours			Customer Lead	
1.4	Define Chart of Accounts	4 hours			Customer Finance	
1.5	Assess data sources	4 hours			Provider Consultant	
1.6	Create data mapping	4 hours			Provider Consultant	
1.7	Finalize project plan	4 hours			Provider PM	
1.8	Requirements sign-off	1 hour			Customer Lead	

4.2 Phase 2: Configuration Tasks

ID	Task	Duration	Start	End	Owner	Status
2.1	Configure company settings	2 hours			Provider	
2.2	Set up fiscal year	1 hour			Provider	
2.3	Import Chart of Accounts	2 hours			Provider	
2.4	Configure VAT settings	2 hours			Provider	
2.5	Configure PAYE settings	2 hours			Provider	
2.6	Create user roles	2 hours			Provider	
2.7	Create user accounts	1 hour			Provider	
2.8	Configure AP module	4 hours			Provider	
2.9	Configure AR module	4 hours			Provider	
2.10	Configure Inventory	4 hours			Provider	
2.11	Configure Sales	4 hours			Provider	
2.12	Configure Purchasing	4 hours			Provider	
2.13	Configure HR & Payroll	8 hours			Provider	
2.14	Configure document templates	4 hours			Provider	
2.15	Configure workflows	4 hours			Provider	
2.16	Set up integrations	8 hours			Provider	
2.17	Configuration review demo	2 hours			Provider	
2.18	Configuration sign-off	1 hour			Customer	

4.3 Phase 3: Data Migration Tasks

ID	Task	Duration	Start	End	Owner	Status
3.1	Prepare migration templates	2 hours			Provider	
3.2	Extract customer data	4 hours			Customer	
3.3	Extract supplier data	4 hours			Customer	
3.4	Extract product data	4 hours			Customer	
3.5	Extract opening balances	4 hours			Customer	
3.6	Extract employee data	4 hours			Customer	
3.7	Transform/cleanse data	8 hours			Provider	
3.8	Test migration (customers)	2 hours			Provider	
3.9	Test migration (suppliers)	2 hours			Provider	
3.10	Test migration (products)	2 hours			Provider	
3.11	Validate test migration	4 hours			Customer	
3.12	Final migration	4 hours			Provider	
3.13	Import opening balances	4 hours			Provider	
3.14	Reconcile trial balance	4 hours			Customer	
3.15	Data migration sign-off	1 hour			Customer	

4.4 Phase 4: Testing Tasks

ID	Task	Duration	Start	End	Owner	Status
4.1	Prepare test scenarios	4 hours			Provider	
4.2	Execute system tests	8 hours			Provider	
4.3	Execute integration tests	4 hours			Provider	
4.4	Prepare UAT environment	2 hours			Provider	
4.5	Conduct UAT briefing	1 hour			Provider	
4.6	Customer executes UAT	16 hours			Customer	
4.7	Log UAT issues	Ongoing			Customer	
4.8	Resolve P1/P2 issues	Varies			Provider	
4.9	Re-test resolved issues	4 hours			Provider	
4.10	UAT sign-off	1 hour			Customer	

4.5 Phase 5: Training Tasks

ID	Task	Duration	Start	End	Owner	Status
5.1	Prepare training environment	2 hours			Provider	
5.2	Customize training materials	4 hours			Provider	
5.3	Admin training	8 hours			Provider	
5.4	Finance training	8 hours			Provider	
5.5	Operations training	4 hours			Provider	
5.6	HR/Payroll training	4 hours			Provider	
5.7	End user training	4 hours			Provider	
5.8	Training assessments	2 hours			Provider	
5.9	Address training gaps	2 hours			Provider	
5.10	Training completion sign-off	1 hour			Customer	

4.6 Phase 6: Go-Live Tasks

ID	Task	Duration	Start	End	Owner	Status
6.1	Complete go-live checklist	4 hours			Both	
6.2	Go-live decision meeting	1 hour			Both	
6.3	Final data cutover	4 hours			Provider	
6.4	Send go-live communication	1 hour			Customer	
6.5	Deactivate old system	1 hour			Customer	
6.6	Begin production transactions	Ongoing			Customer	
6.7	Day 0 support	8 hours			Provider	
6.8	Day 1 support	8 hours			Provider	
6.9	First period close	4 hours			Customer	
6.10	Days 2-5 support	24 hours			Provider	
6.11	Handover to support	2 hours			Provider	
6.12	Project closure meeting	1 hour			Both	
6.13	Project sign-off	1 hour			Customer	

5. Resource Plan

5.1 Provider Team

Role	Name	Allocation	Phase Involvement
Project Manager	[Name]	50%	All phases
Implementation Consultant	[Name]	100%	Phases 1-4
Technical Consultant	[Name]	50%	Phases 2-4
Trainer	[Name]	100%	Phase 5
Support Engineer	[Name]	On-call	Phase 6

5.2 Customer Team

Role	Name	Allocation	Responsibilities
Executive Sponsor	[Name]	10%	Escalations, sign-offs
Project Lead	[Name]	50%	Day-to-day decisions, coordination
IT Contact	[Name]	25%	Technical coordination
Finance Lead	[Name]	50%	Finance configuration, data, UAT
HR Lead	[Name]	25%	HR/Payroll configuration, data
Super Users	[Names]	25%	UAT, training, user support

5.3 Resource Calendar

Week	Provider Hours	Customer Hours	Key Activities
Week 1	40	20	Initiation
Week 2	60	16	Configuration
Week 3	60	16	Configuration
Week 4	40	30	Data Migration
Week 5	40	40	Testing
Week 6	40	40	Training
Week 7	60	40	Go-Live
Total	340	202	

6. Communication Plan


6.1 Regular Meetings

Meeting	Frequency	Day/Time	Duration	Attendees
Status Update	Weekly	[Day] [Time]	30 min	Project Leads
Steering Committee	Bi-weekly	[Day] [Time]	30 min	Sponsors + Leads
Technical Review	Weekly	[Day] [Time]	30 min	Technical Team
Daily Standup (Go-Live)	Daily	[Time]	15 min	Core Team

6.2 Status Reporting

Report	Frequency	Distribution	Owner
Weekly Status Report	Weekly (Friday)	Project Team	Provider PM
Issue Log	Updated continuously	Project Leads	Provider PM
Risk Register	Updated weekly	Steering Committee	Provider PM
Progress Dashboard	Real-time	Project Team	Provider PM

6.3 Escalation Path

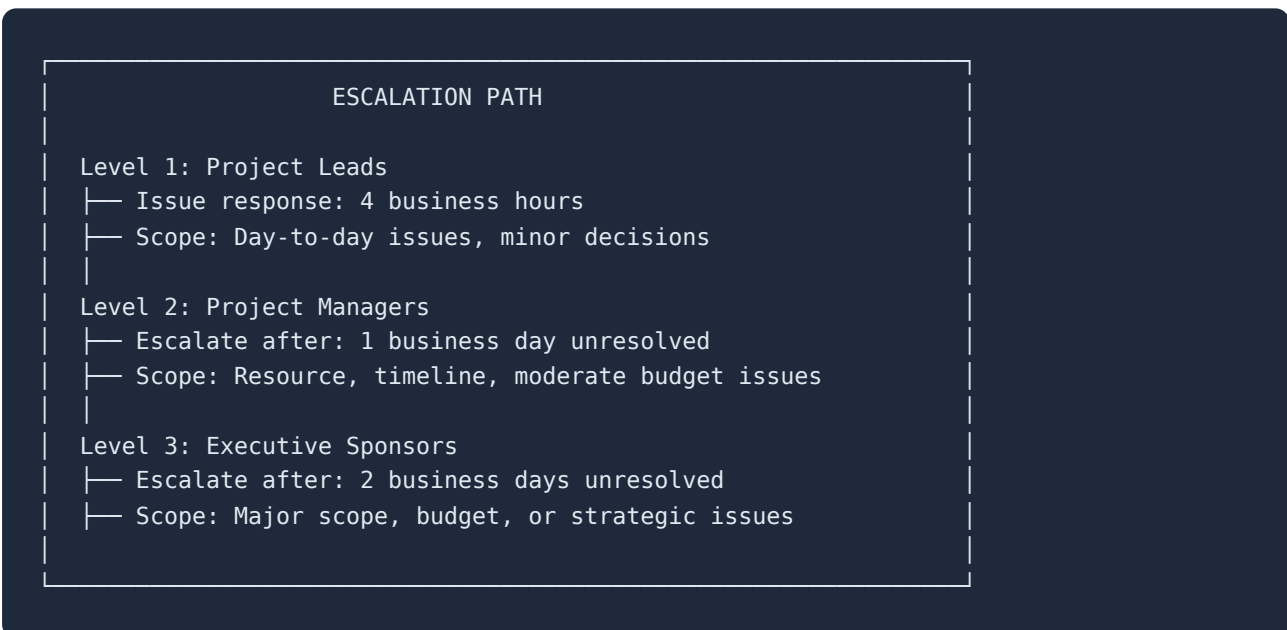

7. Risk Register

ID	Risk	Probability	Impact	Mitigation	Owner	Status
R1	Data quality issues delay migration	Medium	High	Early data assessment; provide templates	Provider	Open
R2	Key resources unavailable	Medium	Medium	Confirm availability upfront; backup resources	Both	Open
R3	Scope creep extends timeline	High	Medium	Strict change control; defer non-critical items	Both	Open
R4	Integration complexity	Low	High	Technical assessment; contingency time	Provider	Open
R5	User adoption challenges	Medium	High	Extra training; change management	Customer	Open
R6	Go-live timing (month-end conflict)	Medium	High	Plan go-live mid-month; avoid year-end	Both	Open
R7	Configuration doesn't meet requirements	Low	High	Weekly demos; iterative approach	Provider	Open
R8	Performance issues	Low	High	Performance testing before go-live	Provider	Open

8. Quality Assurance

8.1 Quality Gates

Gate	Phase	Criteria	Approver
QG1	Initiation	Requirements signed off	Customer Lead
QG2	Configuration	Configuration demo approved	Customer Lead
QG3	Data Migration	Data reconciled to source	Customer Finance
QG4	Testing	UAT passed, no P1/P2 open	Customer Lead
QG5	Training	All users trained, assessments passed	Customer Lead
QG6	Go-Live	Go-live checklist complete	Both Leads
QG7	Closure	Project acceptance signed	Customer Sponsor

8.2 Defect Management

Priority	Definition	Resolution Target
P1 - Critical	System unusable, data loss	4 hours
P2 - High	Major function impaired	1 business day
P3 - Medium	Function impaired, workaround exists	3 business days
P4 - Low	Minor issue, cosmetic	Next release

9. Go-Live Checklist

9.1 Pre-Go-Live (Day -7 to -1)

#	Item	Owner	Date	Status
1	All P1/P2 issues resolved	Provider		
2	UAT signed off	Customer		
3	All users trained	Provider		
4	User accounts created in production	Provider		
5	Production data migrated	Provider		
6	Opening balances reconciled	Customer		
7	Integrations tested in production	Provider		
8	Document templates finalized	Both		
9	Support process communicated	Provider		
10	Go-live communication drafted	Customer		
11	Rollback plan documented	Provider		
12	Go-live decision meeting held	Both		

9.2 Go-Live Day (Day 0)

#	Item	Owner	Time	Status
1	Final data cutover complete	Provider	AM	
2	System access verified for all users	Provider	AM	
3	Go-live communication sent	Customer	AM	
4	Support team on standby	Provider	All day	
5	First transactions processed	Customer	AM	
6	Mid-day check-in	Both	12:00	
7	End-of-day review	Both	17:00	

9.3 Post-Go-Live (Day +1 to +5)

#	Item	Owner	Date	Status
1	Day 1 issues reviewed	Provider		
2	First daily close successful	Customer		
3	Performance monitoring	Provider		
4	User feedback collected	Both		
5	Knowledge transfer sessions	Provider		
6	Handover to support	Provider		
7	First period-end close successful	Customer		
8	Project closure meeting	Both		

10. Project Tracking

10.1 Project Dashboard Template

PROJECT STATUS DASHBOARD

Week Ending: [Date]

OVERALL STATUS:

On Track

At Risk

Off Track

Current Phase: [Phase Name]

% Complete: [X]%

PHASE STATUS

Phase 1 - Initiation:

Complete

Phase 2 - Configuration:

Complete / In Progress

Phase 3 - Data Migration:

Not Started

Phase 4 - Testing:

Not Started

Phase 5 - Training:

Not Started

Phase 6 - Go-Live:

Not Started

KEY METRICS

Tasks Completed:

[X] / [Y]

Open Issues:

[X] (P1: [X], P2: [X], P3: [X])

Risks:

[X] Open

Schedule Variance:

[+/-X] days

THIS WEEK

[Accomplishment 1]

[Accomplishment 2]

NEXT WEEK

[Planned task 1]

[Planned task 2]

BLOCKERS/RISKS

[Issue 1]

[Issue 2]

10.2 Issue Log Template

ID	Date	Description	Priority	Owner	Status	Resolution	Closed
----	------	-------------	----------	-------	--------	------------	--------

10.3 Change Request Log

CR#	Date	Description	Requestor	Impact	Status	Approved By
-----	------	-------------	-----------	--------	--------	-------------

Appendices

Appendix A: Glossary

Term	Definition
AP	Accounts Payable
AR	Accounts Receivable
BOM	Bill of Materials
CoA	Chart of Accounts
CRM	Customer Relationship Management
GL	General Ledger
GRN	Goods Received Note
MSA	Master Services Agreement
PAYE	Pay As You Earn
PO	Purchase Order
SARS	South African Revenue Service
SLA	Service Level Agreement
SO	Sales Order
SOW	Statement of Work
UAT	User Acceptance Testing
VAT	Value Added Tax

Appendix B: Document Templates

- Configuration Workbook
- Data Migration Templates
- Test Case Template
- Issue Log Template
- Change Request Form
- Training Attendance Sheet
- Sign-off Forms

Appendix C: Contact List

[Attach complete contact list with all project team members]

Document Control

Version	Date	Author	Changes
1.0	January 2026	Professional Services	Initial template

SiyaBusa ERP - Powering African Business

© 2026 Masaphokati Technologies (Pty) Ltd. All Rights Reserved.
