

SiyaBusa ERP

SOW TEMPLATE

Sales Enablement

Masaphokati Technologies (Pty) Ltd

Document Version: 1.0

Effective Date: January 2026

Department: Sales

Classification: Confidential

WE RULE. WE GOVERN. WE EMPOWER.

Statement of Work (SOW)

CONTRACT TEMPLATE

Statement of work template for implementation projects.

SiyaBusa ERP Implementation

Document Header

Field	Value
SOW Number	SOW-[YEAR]-[NUMBER]
Customer Name	[Customer Legal Name]
Project Name	SiyaBusa ERP Implementation
Prepared By	[Sales Rep Name]
Prepared Date	[Date]
Valid Until	[Date + 30 days]

1. Executive Summary

1.1 Purpose

This Statement of Work (SOW) describes the implementation services to be provided by Masaphokati Technologies (Pty) Ltd ("Provider" or "Masaphokati") to [Customer Name] ("Customer" or "Client") for the deployment and configuration of the SiyaBusa ERP system.

1.2 Project Overview

[Brief description of the project - customize per customer]

Example:

This SOW covers the implementation of SiyaBusa ERP Professional plan for [Customer Name], including configuration of Financial Accounting, Inventory Management, HR &

Payroll, and SARS compliance modules. The project will migrate 3 years of historical data from the existing [System Name] system and provide comprehensive training to 25 end users.

1.3 Project Objectives

#	Objective
1	Deploy and configure SiyaBusa ERP for [Customer Name]
2	Migrate historical data from [Current System]
3	Configure modules: [List modules]
4	Integrate with: [List integrations]
5	Train [X] end users and [X] administrators
6	Achieve go-live by [Target Date]

2. Scope of Work

2.1 In-Scope Services

2.1.1 Project Management

Service	Description
Project Planning	Detailed project plan with milestones
Status Reporting	Weekly status reports and meetings
Issue Management	Issue tracking and resolution
Change Management	Change request process
Risk Management	Risk identification and mitigation

2.1.2 System Configuration

Module	Configuration Activities
Core Setup	Company setup, Chart of Accounts, fiscal year, tax settings
Financial Accounting	GL structure, journal templates, reporting periods
Accounts Payable	Supplier setup, payment terms, approval workflows
Accounts Receivable	Customer setup, credit terms, aging buckets
Inventory	Products, categories, warehouses, units of measure
Sales	Pricing, discounts, sales processes, document templates
Purchasing	PO workflows, receiving, three-way match
HR & Payroll	Employee setup, pay structures, deductions, leave policies
SARS Integration	VAT setup, PAYE configuration, submission schedules
User Setup	Roles, permissions, user accounts

2.1.3 Data Migration

Data Type	Records	Migration Method
Chart of Accounts	[X] accounts	Template import
Customers	[X] records	API/Template
Suppliers	[X] records	API/Template
Products	[X] SKUs	API/Template
Opening Balances	As of [Date]	Journal entry
Historical Transactions	[X] years	Bulk import
Employees	[X] records	Template import

2.1.4 Integrations

System	Integration Type	Direction
[System 1]	API	Bi-directional
[Bank Name]	Bank feeds	Inbound
[E-commerce]	API	Inbound

2.1.5 Custom Development (if applicable)

Item	Description	Estimated Effort
Custom Report 1	[Description]	[X] hours
Custom Report 2	[Description]	[X] hours
Custom Integration	[Description]	[X] hours

2.1.6 Training

Training Type	Audience	Duration	Delivery
System Administration	IT/Admin (2-3 people)	8 hours	Virtual
Finance Training	Finance team (X people)	8 hours	Virtual
Sales/Inventory	Operations (X people)	4 hours	Virtual
HR/Payroll	HR team (X people)	4 hours	Virtual
End User Training	All users (X people)	4 hours	Virtual

2.1.7 Go-Live Support

Service	Duration	Description
Pre-Go-Live	2 days	Final testing, data validation
Go-Live Day	1 day	On-call support (virtual)
Post-Go-Live	5 business days	Priority support, issue resolution

2.2 Out-of-Scope

The following items are explicitly **NOT** included in this SOW:

#	Item	Notes
1	Hardware procurement	Customer responsibility
2	Network infrastructure	Customer responsibility
3	Custom module development	Requires separate SOW
4	Third-party software licenses	Customer responsibility
5	Data cleansing/enrichment	Available as add-on
6	On-site services	Available as add-on
7	Historical data beyond [X] years	Available as add-on
8	Training beyond specified hours	Available as add-on

3. Deliverables

3.1 Deliverables List

#	Deliverable	Description	Format
D1	Project Plan	Detailed timeline with milestones	MS Project/PDF
D2	Configuration Workbook	Documented configuration decisions	Excel
D3	Data Migration Report	Validation of migrated data	PDF
D4	Test Results	UAT test cases and results	Excel/PDF
D5	Training Materials	User guides, quick reference	PDF
D6	Training Completion	Sign-off sheets	PDF
D7	Go-Live Checklist	Completed go-live validation	PDF
D8	Project Closure Report	Final project summary	PDF

3.2 Acceptance Criteria

Each deliverable will be considered accepted when:

1. Deliverable is provided to Customer

2. Customer has 5 business days to review
 3. Customer provides written acceptance OR
 4. Customer does not respond within 5 business days (deemed accepted) OR
 5. Customer provides specific feedback for revision
-

4. Project Timeline

4.1 Project Schedule

Phase	Duration	Start Date	End Date
Phase 1: Initiation	1 week	[Date]	[Date]
Kickoff meeting			
Project planning			
Requirements confirmation			
Phase 2: Configuration	2 weeks	[Date]	[Date]
Core system setup			
Module configuration			
Workflow setup			
Phase 3: Data Migration	1 week	[Date]	[Date]
Data mapping			
Data extraction & transformation			
Data loading & validation			
Phase 4: Testing	1 week	[Date]	[Date]
System testing			
Integration testing			
User acceptance testing			
Phase 5: Training	1 week	[Date]	[Date]
Admin training			
End user training			
Phase 6: Go-Live	1 week	[Date]	[Date]
Final preparation			
Go-live execution			

Phase	Duration	Start Date	End Date
Post-go-live support			
Total Duration	[X] weeks	[Date]	[Date]

4.2 Key Milestones

Milestone	Target Date	Success Criteria
M1: Project Kickoff	[Date]	Kickoff complete, plan approved
M2: Configuration Complete	[Date]	All modules configured
M3: Data Migration Complete	[Date]	Data validated, balances reconciled
M4: UAT Sign-off	[Date]	All test cases passed
M5: Training Complete	[Date]	All users trained
M6: Go-Live	[Date]	System live, users transacting
M7: Project Closure	[Date]	Project accepted, SOW complete

5. Pricing & Payment

5.1 Service Fees

Service	Unit	Qty	Unit Price	Total
Subscription (Annual)				
SiyaBusa ERP [Plan]	Per year	1	R[X]	R[X]
Additional Users	Per user/year	[X]	R[X]	R[X]
Implementation Services				
[Package] Implementation	Fixed	1	R[X]	R[X]
Data Migration (Extended)	Per item	[X]	R[X]	R[X]
Custom Report Development	Per report	[X]	R[X]	R[X]
Integration Development	Per integration	[X]	R[X]	R[X]
Additional Training	Per hour	[X]	R[X]	R[X]
Subtotal				R[X]
Discount ([X]%)				-R[X]
VAT (15%)				R[X]
Total				R[X]

5.2 Payment Schedule

Milestone	Amount	Due Date
SOW Signing (Deposit)	50% of Implementation	Upon signing
Go-Live	50% of Implementation	At go-live
Annual Subscription	100%	Upon signing (or monthly)

5.3 Payment Terms

- **Payment Due:** Net 14 days from invoice date
- **Late Payment:** 2% per month interest on overdue amounts

- **Currency:** South African Rand (ZAR)
 - **Payment Method:** EFT / Credit Card / Debit Order
-

6. Assumptions

6.1 Customer Assumptions

#	Assumption
A1	Customer will provide timely access to required systems and data
A2	Customer will assign a dedicated project lead with decision authority
A3	Customer will provide clean, accurate data in required format
A4	Customer users will be available for scheduled training sessions
A5	Customer will provide feedback within 5 business days of requests
A6	Customer has stable internet connectivity (minimum 10 Mbps)
A7	Customer will use modern web browsers (Chrome, Edge, Safari - latest versions)
A8	Customer's existing data is complete and reconciled

6.2 Provider Assumptions

#	Assumption
A9	Provider will have access to Customer systems during business hours
A10	Provider resources will work remotely unless otherwise specified
A11	Implementation uses standard SiyaBusa functionality
A12	Data migration volume as specified in Section 2.1.3

7. Roles & Responsibilities

7.1 Provider Responsibilities

Role	Name	Responsibilities
Project Manager	[Name]	Overall project delivery, status reporting, escalations
Implementation Consultant	[Name]	System configuration, data migration
Technical Lead	[Name]	Integrations, technical issues
Trainer	[Name]	Training delivery
Support Contact	Support Team	Ongoing support post-implementation

7.2 Customer Responsibilities

Role	Name	Responsibilities
Executive Sponsor	[Name]	Executive oversight, escalation point
Project Lead	[Name]	Day-to-day decisions, resource coordination
IT Contact	[Name]	Technical coordination, access management
Finance Lead	[Name]	Finance requirements, data validation
HR Lead	[Name]	HR/Payroll requirements, data validation
Super Users	[Names]	Testing, training attendance, user support

7.3 RACI Matrix


Activity	Provider PM	Provider Team	Customer Lead	Customer Team
Project Planning	R	C	A	I
Requirements Gathering	R	C	A	C
System Configuration	A	R	C	I
Data Preparation	C	C	A	R
Data Migration	A	R	C	I
Testing	C	R	A	R
Training	A	R	C	R
Go-Live	R	R	A	R
UAT Sign-off	I	I	A	R

R=Responsible, **A**=Accountable, **C**=Consulted, **I**=Informed

8. Change Management

8.1 Change Request Process

Changes to this SOW must follow this process:

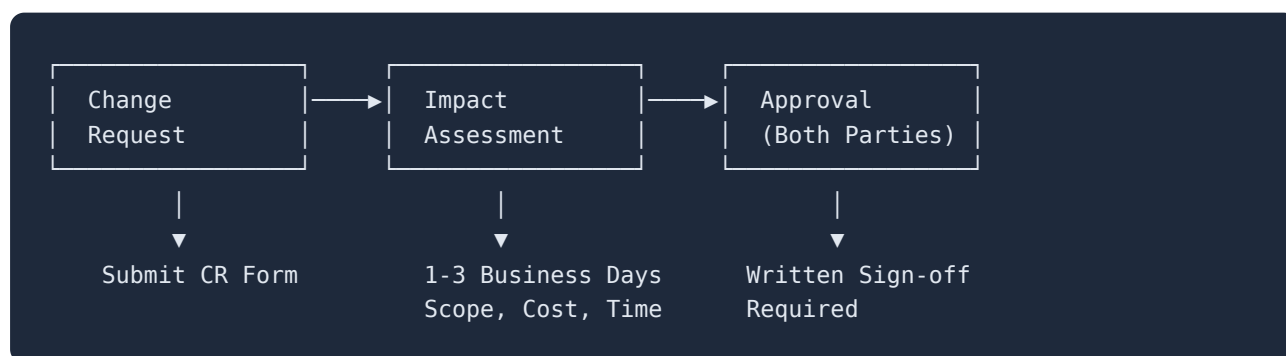

8.2 Change Request Form

Changes will be documented using a Change Request Form including:

- Change description

- Business justification
- Scope impact
- Cost impact
- Schedule impact
- Approval signatures

8.3 Change Approval Authority

Change Impact	Approval Required
< R10,000 / < 1 week	Project Leads (both parties)
R10,000 - R50,000 / 1-4 weeks	Executive Sponsors
> R50,000 / > 4 weeks	Contract Amendment

9. Risk Management

9.1 Identified Risks

#	Risk	Probability	Impact	Mitigation
R1	Data quality issues	Medium	High	Early data assessment, cleansing support
R2	Resource availability	Medium	Medium	Confirm availability before kickoff
R3	Scope creep	High	Medium	Strict change management process
R4	Integration complexity	Low	High	Technical assessment, contingency time
R5	User adoption	Medium	High	Training, change management support
R6	Go-live timing (month-end)	Medium	High	Avoid month-end/year-end go-live

9.2 Risk Response

Risks will be tracked in a risk register and reviewed weekly. Significant risks will be escalated to Executive Sponsors.

10. Communication Plan

10.1 Regular Communications

Communication	Frequency	Attendees	Format
Status Report	Weekly	Project Leads	Email
Status Meeting	Weekly	Project Teams	Virtual (30 min)
Steering Committee	Bi-weekly	Executives	Virtual (30 min)
Issue Escalation	As needed	As appropriate	Email/Call

10.2 Key Contacts

Role	Name	Email	Phone
Provider PM	[Name]	[Email]	[Phone]
Provider Support	Support Team	support@siyabusa.com	[Phone]
Customer Lead	[Name]	[Email]	[Phone]
Customer Sponsor	[Name]	[Email]	[Phone]

11. Terms & Conditions

11.1 Term

This SOW is effective from the date of last signature and remains in effect until project completion or termination.

11.2 Termination

Either party may terminate this SOW with 30 days written notice. In case of termination:

- Customer pays for work completed to date
- Provider delivers all work product completed
- Subscription terms per Master Agreement

11.3 Warranty

Provider warrants that:

- Services will be performed professionally
- System will function as documented
- Implementation defects will be corrected at no charge for 30 days post go-live

11.4 Limitation of Liability

Provider's total liability under this SOW shall not exceed the total fees paid under this SOW.

11.5 Confidentiality

Both parties agree to maintain confidentiality of the other party's proprietary information.

11.6 Governing Law

This SOW shall be governed by the laws of the Republic of South Africa.

11.7 Master Agreement

This SOW is subject to the terms of the SiyaBusa ERP Master Services Agreement. In case of conflict, the MSA prevails.

12. Signatures

Provider: Masaphokati Technologies (Pty) Ltd

Field	Value
Authorized Signatory	
Name	
Title	
Date	

Customer: [Customer Legal Name]

Field	Value
Authorized Signatory	
Name	
Title	
Date	

Appendix A: Detailed Configuration Checklist

[Attach detailed configuration checklist based on customer requirements]

Appendix B: Data Migration Specifications

[Attach detailed data mapping and migration specifications]

Appendix C: Integration Specifications

[Attach detailed integration requirements and specifications]

Appendix D: Training Curriculum

[Attach detailed training agenda and materials list]

Document Control

Version	Date	Author	Changes
1.0	[Date]	[Name]	Initial SOW

SiyaBusa ERP - Powering African Business

© 2026 Masaphokati Technologies (Pty) Ltd. All Rights Reserved.
